

THE GARAGE

Construction Update

Issue 39 – 25th September 2020



General progress

Work on site is progressing well and is moving inside over the next weeks as roofs to all buildings are being completed and soon to be followed by windows installation.



Work concluded this week

- Copings installed to Parfitt and scaffold lowered to enable install of rear roof
- Slates and sarnofil (flat roof) installation has started on Preedy
- Internal hot and cold water distribution to Preedy continued
- Connection of shower pods to hot, cold and soil pipes continued
- Brick and block work towards roof level continued on Townsend and Beddoe
- Roof carpentry and trusses installation commenced on MacDonald



Work planned for coming week

- Reduce scaffold to Parfitt further to enable ground floor roof installation
- Start installation of windows to Parfitt
- Continue slate installation and sarnofil works to roof of Preedy
- Start roof carpentry work to Beddoe
- Complete roof works on MacDonald and start brick work on parapets
- All blocks - Continue with water distribution and shower room connections
- All blocks - Enabling works for electrical installation will start



Any noisy work planned this week?

Due to the brick finish to the gable ends of the buildings, there will still be some noise from the much hated brick cutting machine.

SITE CONTACT:

Keith Holt (temp. site manager) 07514 496 703 keith.holt@hgconstruction.co.uk
 Graham Fisher (project manager) 07972 136 505 graham.fisher@hgconstruction.co.uk
 Mark Yonwin (Danehurst) 07788 561 159 mark@danehurst.com
 Emergency out of hours contact: 0870 720 0785

HG CONSTRUCTION LTD

4 Hunting Gate Hitchin Hertfordshire SG4 0TJ
 01462 454444
 www.hgconstruction.co.uk




Parking

The parking monitor has not identified any vehicles belonging to site parking in the nearby streets and no vehicles have been reported to us.

Progress Photos



The hoarding will be updated to include new images of the development

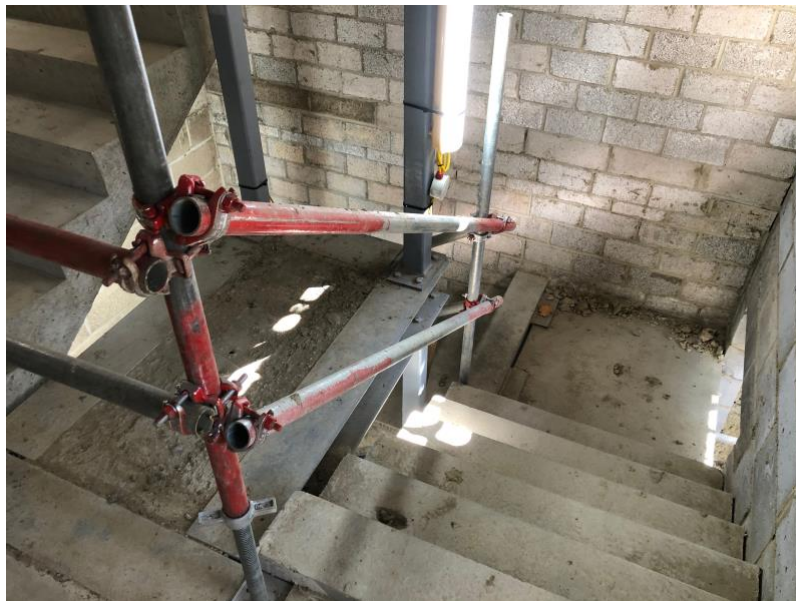

Staircases are now installed to all buildings

SITE CONTACT:

Keith Holt (temp. site manager) 07514 496 703 keith.holt@hgconstruction.co.uk
 Graham Fisher (project manager) 07972 136 505 graham.fisher@hgconstruction.co.uk
 Mark Yonwin (Danehurst) 07788 561 159 mark@danehurst.com
 Emergency out of hours contact: 0870 720 0785

HG CONSTRUCTION LTD
 4 Hunting Gate Hitchin Hertfordshire SG4 0TJ
 01462 454444
 www.hgconstruction.co.uk



This will eventually become the common room in lower ground floor of Townsend



And it will end up looking something like this...and will be known as

THE BODYSHOP

In keeping with The Garage theme!
